
MANAGEKARO · ERP · HRM · PROJECTS

The Managekaro User Book

Every module, every department, every workflow — for interior fit-out and construction companies.

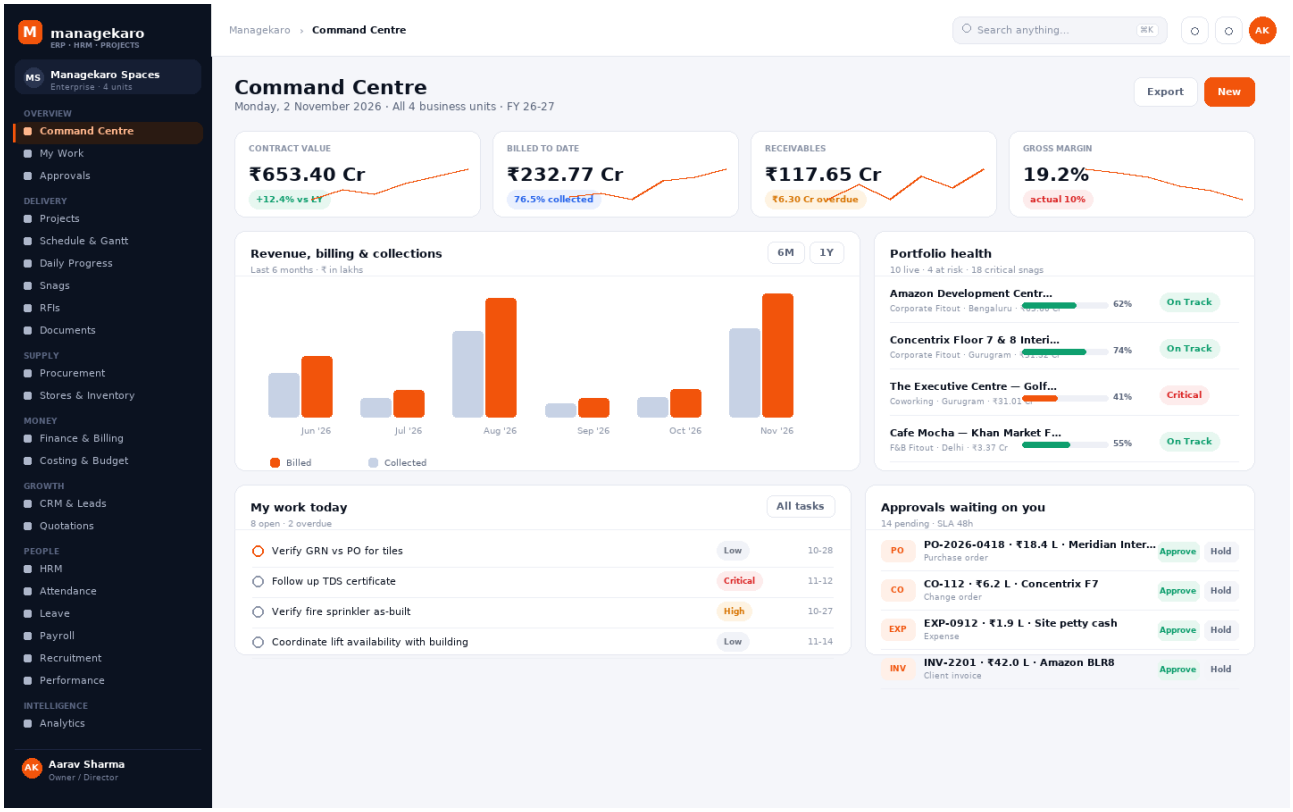

Version 1.0 · 2 November 2026 · 14 chapters · 71 topics

Contents

Read chapters 1–3 for setup and project control, 4–7 for execution and commercials, 8–9 for growth and people, 10 for intelligence, and 11–14 for administration, roles and deployment.

01	1. Getting started	4 topics
02	2. Command Centre & My Work	4 topics
03	3. Projects & BOQ	7 topics
04	4. Schedule, Gantt & daily progress	7 topics
05	5. Drawings & documents	3 topics
06	6. Procurement & stores	7 topics
07	7. Finance, billing & costing	7 topics
08	8. CRM & quotations	5 topics
09	9. HRM & payroll	7 topics
10	10. Analytics, Copilot & agents	4 topics
11	11. Admin, masters & billing	6 topics
12	12. Roles: who does what	3 topics
13	13. Desktop app & deployment	4 topics
14	14. Glossary & shortcuts	3 topics

01

1. Getting started

Managekaro is a single workspace for interior fit-out and construction companies. It connects commercial control (BOQ, procurement, billing) with execution (schedule, DPR, snags, drawings) and people (attendance, leave, payroll). Every record links to a project and, wherever relevant, to a BOQ line — so cost, progress and quality can be read together.

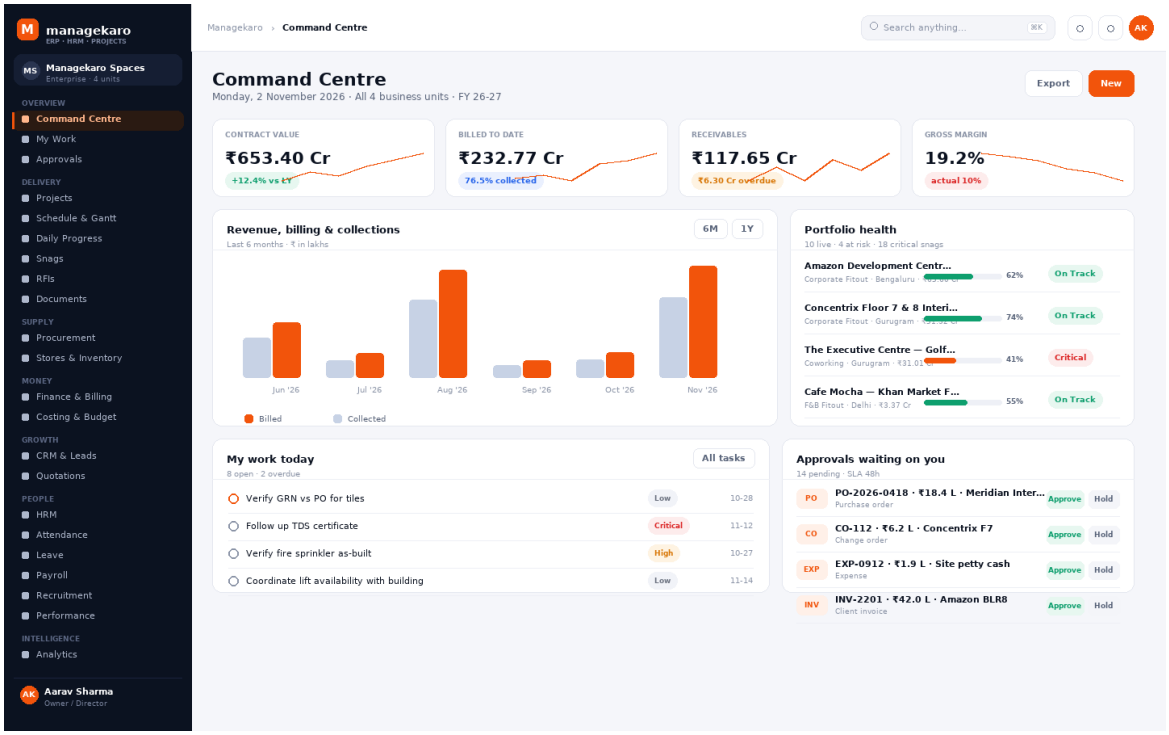


Figure 1.1 — Command Centre: contract value, billing, receivables and margin for the whole portfolio.

1.2 Signing in

Open the workspace and choose a persona on the sign-in screen: Director, Project Manager, Procurement, Finance, Site Engineer or HR Manager. In production this screen is replaced by your SSO / email OTP provider. Role determines menus, approvals and data scope.

1.3 The layout

Left: module navigation grouped by Overview, Delivery, Commercial, Growth, People, Intelligence and Admin. Top: breadcrumb, global search (⌘K), download shortcut, notifications and the user switcher. Main area: the module screen.

1.4 Your first 60 minutes

1) Verify organisation profile and GSTIN in Settings. 2) Import clients, vendors and item master. 3) Create one project and import its BOQ. 4) Invite your PM, QS, procurement and finance leads with the right roles. 5) Raise one test PO, receive it (GRN) and match an invoice. 6) Ask your site engineer to submit a DPR from a phone.

1.5 The demo dataset

The workspace ships with a complete, deterministic demo company: 16 projects, 57 employees, live BOQ lines, purchase orders, invoices, payroll and snags, all pinned to a fixed seed so every screen looks identical for every user. Nothing you see is a mock-up — KPIs, charts and tables are computed from that dataset. Reset it any time from Settings → Data & backup → Reset demo data.

1.6 Department map — who works where

Department	Owns in Managekaro	Primary screens
Leadership	Portfolio value, margin, cash, risk	Command Centre, Analytics, Approvals
Sales & CRM	Leads, site surveys, quotations, win rate	CRM & Leads, Quotations
Design & Studio	Drawings, revisions, GFC approvals, design BOQ	Project → Design, Documents
Projects & Site	WBS, schedule, DPR, snags, RFIs, handover	Schedule, DPR, Snags, RFIs
Quantity Surveying	BOQ, variations, change orders, certification	Project → BOQ & Scope
Procurement & Stores	Indents, RFQs, POs, GRN, stock, vendors	Procurement, Stores & Inventory
Finance & Accounts	Invoices, retention, TDS, GST, payables, cash	Finance & Billing, Costing
HR & Admin	Hiring, attendance, leave, payroll, appraisals	HRM, Attendance, Payroll

1.7 The problems this replaces

- Excel BOQ drift — every revision lives in a new file, so certified value, variations and margin disagree. Managekaro keeps one BOQ per project with executed quantity and variance on every line.
- WhatsApp DPRs — progress and photos arrive in six groups and never reach billing. DPRs are linked to schedule activities and feed certification.
- Procurement leakage — ordered vs received vs billed is reconciled by hand at month-end. Three-way match and committed-cost tracking close that gap daily.
- Billing lag — milestones are certified but not invoiced for weeks. The billing tab always shows certified-but-not-invoiced value per project.
- Payroll & attendance chaos — muster rolls for site labour and a separate register for staff. One attendance engine feeds both.
- No single truth for the founder — six spreadsheets and three versions of the pipeline. The Command Centre recomputes from transactions, never from typed-in summaries.

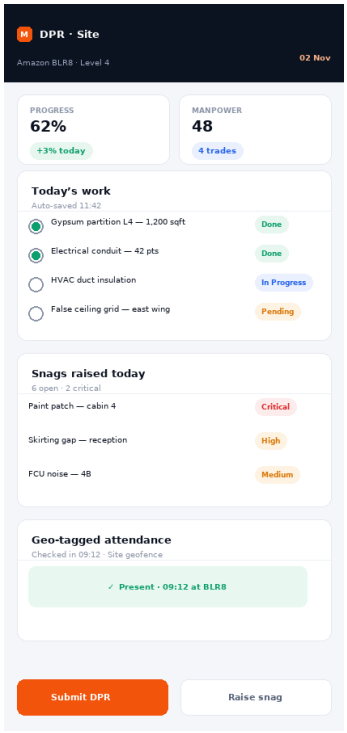


Figure 1.2 — The same workspace on a site engineer's phone: DPR, snags and geo-tagged attendance.

02

2. Command Centre & My Work

The landing screen for leadership. KPI row: contract value, collected, projected profit and at-risk projects. Second row covers payables, overdue receivables, headcount, pipeline and pending approvals. Charts show planned vs actual portfolio progress, portfolio health split and cash position. Tables list live projects with progress, contract, collected, margin and health.

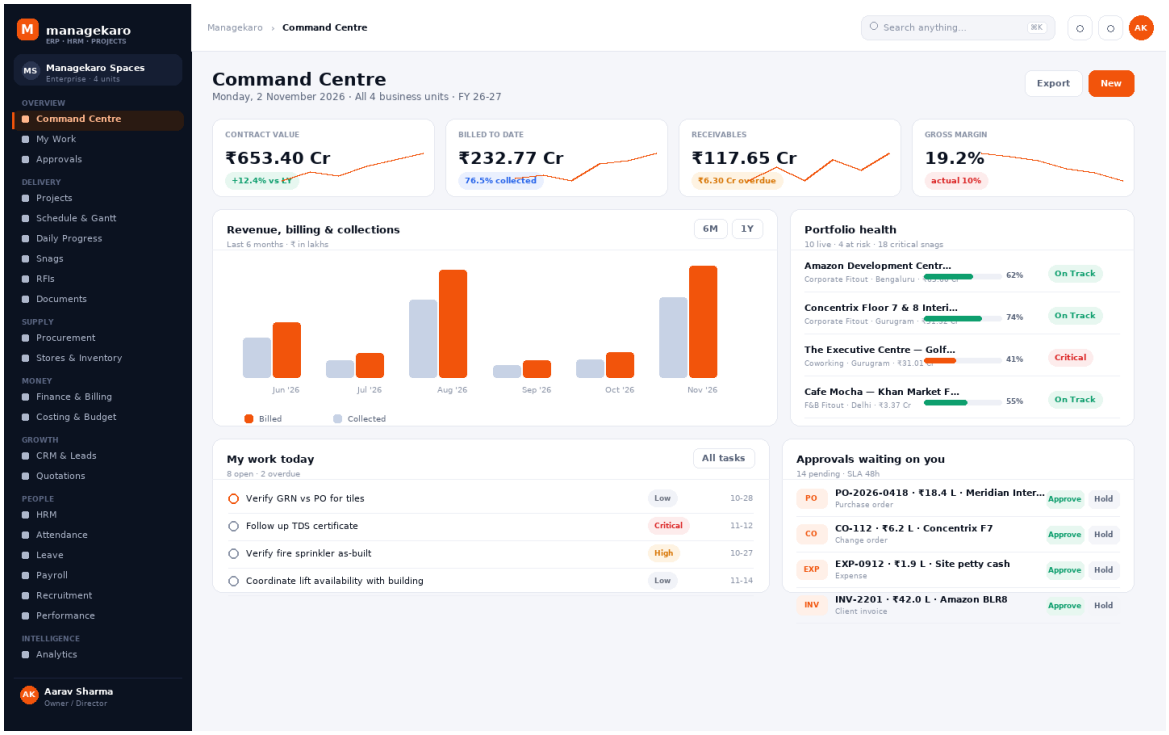


Figure 2.1 — Portfolio health, today’s work and the approvals waiting on you.

2.2 Exporting an MIS pack

Click "Export MIS" to download a CSV of portfolio KPIs, or use Analytics → Export data for a project-level file. Subscribe from Analytics → Subscribe MIS to receive a scheduled pack by email or WhatsApp.

2.3 My Work

Your personal queue: tasks, approvals waiting, leave balance and today's attendance. Switch between List and Board (kanban). "New task" creates a contextual task linked to a project, with priority and due date.

2.4 Approvals inbox

Every document routed to you appears here with amount, project, requester, level (e.g. L1 of 3) and SLA. Approve or reject with a comment; approving a PO releases it to the vendor, approving a change order updates the project's revised value. Bulk approve is available for low-risk batches.

2.5 My Work

Every user gets a personal queue: tasks assigned to them across projects, DPRs awaiting review, approvals in their name, snags they own and RFIs they must answer. Overdue items sort to the top

with a red SLA chip, and any row deep-links into the record. Filter by project, module or due window.

2.6 Approvals inbox

Amount-based hierarchy: a PO under ₹5 L goes to the Project Manager, ₹5–25 L to the Head of Procurement, above ₹25 L to the Founder / CFO. Each request shows type, reference, amount, level (for example L2 of 3), SLA and the full trail. Actions: approve, reject with reason, request changes, or delegate. Bulk actions work on multi-select for related documents.

2.7 Notifications & the command palette

The bell collects approvals, mentions, SLA breaches, low-stock alerts and payroll confirmations. ⌘K / Ctrl+K opens the palette: type a project code, employee name, vendor, invoice number or module name and jump straight there; actions such as “new purchase order” or “run payroll” are searchable too.

2.8 Exporting an MIS pack

Use the export button on any list to download exactly the rows and columns you filtered. Analytics → Export gives a project-level file; scheduled MIS subscriptions deliver the same pack by email or WhatsApp on a cadence you set.

03

3. Projects & BOQ

Projects → New project. Capture client, type (corporate, retail, F&B, healthcare, hospitality, residential, commercial, industrial, coworking), city, unit, contract value, area, start and handover dates, PM and budget %. Managekaro creates the project shell, a BOQ template, schedule skeleton, milestones and client portal access.

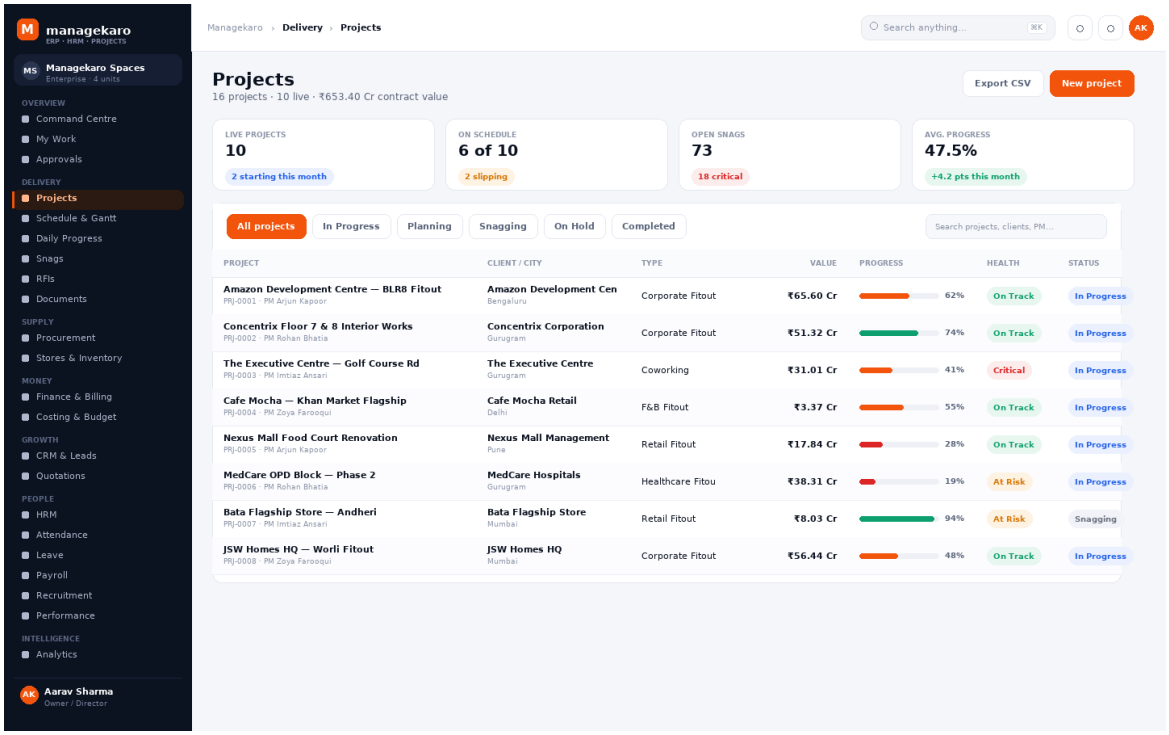


Figure 3.1 — Projects list with health, progress and contract value at a glance.

3.2 The project screen

Nine tabs: Overview, BOQ & scope, Schedule, Procurement, Commercials, Snags & quality, Drawings, Team and Activity. Overview shows execution rings (schedule, BOQ executed, collection), top BOQ lines, project facts, cost mix, milestones, critical snags and recent activity.

3.3 BOQ — the anchor

Each line has WBS code, trade, description, quantity, unit, rate, amount, executed quantity, certified quantity, ordered quantity, progress, budget rate and variance. Client confirmation is tracked per line. Use "Export BOQ" for the client, "Add line" for new scope and "Raise change order" for variations.

3.4 Reading variance

Variance = (ordered rate − budget rate) × quantity. Positive variance is margin leakage — the line was bought above budget. Managekaro surfaces the largest leaks in Cost & Margin so you can renegotiate before month end.

3.5 Change orders

Raise a variation with type (addition / omission / substitution), amount, schedule impact (days), linked BOQ line and justification. It enters the approval chain and, once client-approved, increases

the revised contract value used in P&L.

3.6 Client status report

Project → Client report produces a printable pack: KPI strip, activity-wise progress, client-facing snags and billing summary — ready to save as PDF or email.

3.7 Portfolio view

Projects → Portfolio view compares live projects by value, progress and cash gap, with a value split chart. Print it for the leadership review.

3.8 The nine project tabs

Tab	What lives there
Overview	Health, progress, key dates, team, risks, recent activity
BOQ & Scope	Line items by WBS and trade, executed quantity, variance, change orders
Schedule	Activities with baseline vs actual, dependencies, milestones, delays
Design & Drawings	Drawing register, revision history, GFC status, pin comments
Procurement	Indents, POs and GRNs for this project, committed vs budget
DPR	Daily reports with manpower, work done, blockers and photos
Snags	Issue list with trade, priority, owner and proof of resolution
Billing	Milestones, invoices, retention, TDS, collection status
Documents	Contracts, approvals, checklists, handover pack

3.9 BOQ hygiene the app enforces

- Every line needs a WBS code, trade, unit, quantity and rate — blank cells are rejected on import.
- Executed quantity cannot exceed BOQ quantity unless a change order is approved first.
- Rate variance above the budget rate is highlighted, and the copilot reports leakage per trade.
- Certified value rolls into the billing tab, so “certified but not invoiced” is always visible.

3.10 Change orders

Raise a CO against a project (optionally against a BOQ line), attach justification and client approval, route it through the approval matrix, then apply it. Applied COs increase contract value and create the matching BOQ lines, so billing stays aligned with what was actually built.

3.11 Creating a project

New project asks for client, type (corporate fit-out, coworking, retail, F&B, healthcare, civil), city, contract value, start and end dates, PM and site engineer. It creates the project code, the default tab set and an empty BOQ. Import the BOQ from CSV or build it from a template — both keep WBS and trade structure intact.

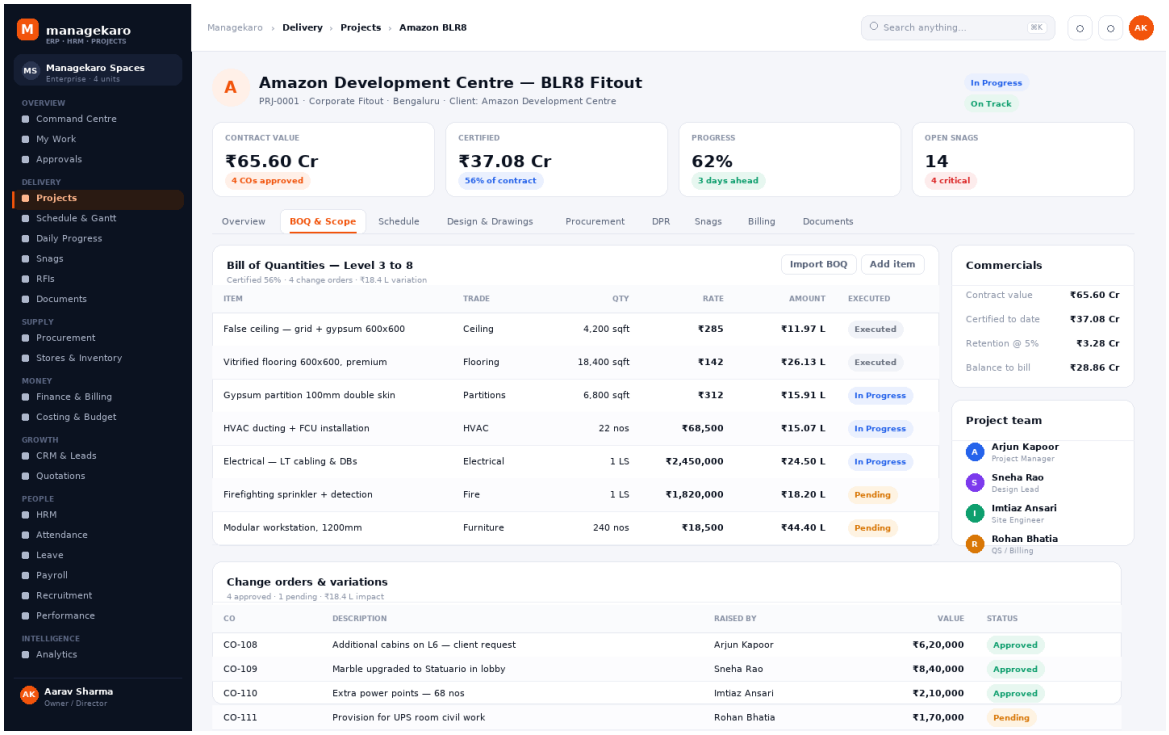


Figure 3.2 — Project detail → BOQ & scope, with change orders underneath.

04

4. Schedule, Gantt & daily progress

Every activity carries trade, start, finish, baseline start and finish, weight, progress, owner, dependency and milestone flag. Weighted progress rolls up to the project percentage.

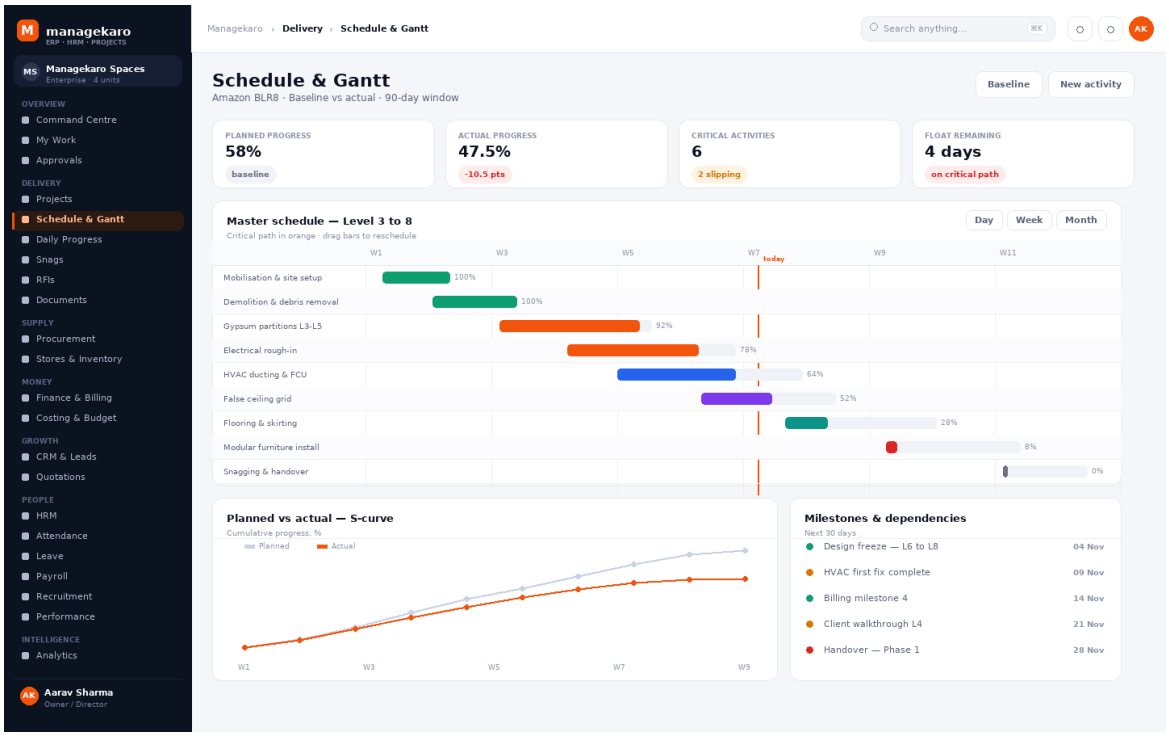


Figure 4.1 — Schedule & Gantt with baseline, S-curve, slipping activities and milestones.

4.2 Gantt

Bars show actual duration with a baseline bar behind and a milestone diamond at completion. Colour: grey baseline, orange in progress, green complete, red slipping. Slipping activities appear in the Delay register with slack days.

4.3 Importing a schedule

Import MS Project XML, Primavera XER or CSV. Managekaro maps ID, name, start, finish, percent complete, predecessor and weight, then builds the baseline.

4.4 Daily Progress Report (DPR)

DPR captures date, manpower (skilled / helpers), progress %, work done, blockers, material inward / outward, safety incidents, weather, photos and quality self-score. Submitting distributes a branded report to client subscribers on WhatsApp and email.

4.5 DPR quality gates

Configure required sections in Settings → DPR & templates, require at least one photograph, and choose whether cost data is included in the client copy.

4.6 Snags

Raise a snag with area, trade, description, priority, committed closure date, vendor assignment and client visibility. The resolution workflow is: raised → assigned → vendor submits proof → QC verifies → closed. Overdue snags are highlighted in Command Centre.

4.7 RFIs

Log technical queries with the addressee (client, PMC, design studio, structural consultant), response due date, and cost / time impact. Answered RFIs remain linked to the project for the final handover pack.

4.8 Reading the Gantt

- Grey bar = baseline; coloured bar = actual progress to date.
- Orange = critical path; a red dot marks an activity already late against its baseline finish.
- The vertical line is today — bars to its right are future work.
- The S-curve compares cumulative planned vs actual progress; the gap between the curves is your slippage.

4.9 Submitting a DPR from site

A site engineer opens Daily Progress on a phone, picks the project and records manpower by trade, work done per activity, material received, blockers and up to nine photos. Submitting time-stamps the report, geo-tags it when permission is granted and notifies the PM. Reviewed DPRs update activity progress, which updates the Gantt and the project progress KPI.

4.10 Snags, RFIs and documents

Snags carry trade, location, priority, owner, due date and a photo; closure needs a resolution photo, so vendors cannot self-certify. RFIs track questions to consultants with due dates, and the answer is attached to the drawing revision it affects. The document register keeps contracts, drawings and approvals with revision numbers and pin comments.

4.11 Delay register

Any activity whose actual finish runs past baseline lands in the delay register with reason codes (design change, material delay, labour, client decision, weather). Reasons roll up into the delivery analytics tab, which is what you quote in a client delay discussion.

05

5. Drawings & documents

Each drawing sheet keeps one current revision; older revisions are marked Superseded, never deleted. Uploading a new revision creates a transmittal entry and notifies subscribers.

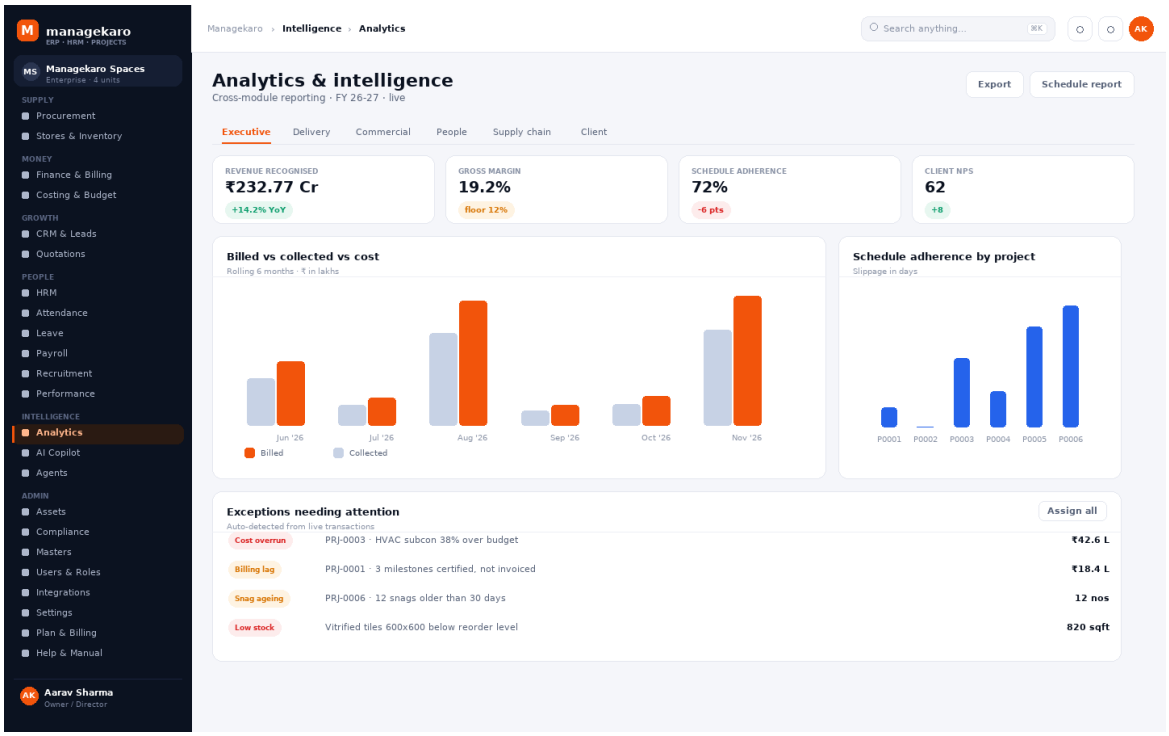


Figure 5.1 — Cross-module analytics: every drawing, DPR and cost line can be sliced here.

5.2 Review & pin comments

Review a drawing, add pin comments at coordinates and record your decision. Approved drawings can be auto-shared to the client portal.

5.3 Sharing

Client-shared documents appear in the client portal. Vendors receive only the sheets attached to their scope.

5.4 Document control rules

- One register per project: contracts, drawings, approvals, checklists and the handover pack.
- Every drawing has a revision number, issue date, status (WIP / For review / GFC / As-built) and pin comments.
- Search by number, title, tag or issuer — results stay project-scoped by default.
- Nothing is deleted: superseded revisions remain visible as history, which matters in a dispute.

5.5 Handover pack

At completion, the handover pack assembles as-built drawings, O&M manuals, warranties, test certificates, snag-closure evidence and the final bill. Export it as a single PDF per project — the

same pack a client's facility team asks for six months later.

06

6. Procurement & stores

Requisition (PR) → approval → vendor selection → purchase order (PO) → goods receipt (GRN) → vendor invoice → 3-way match → payment. Each step is traceable back to the project and BOQ line.

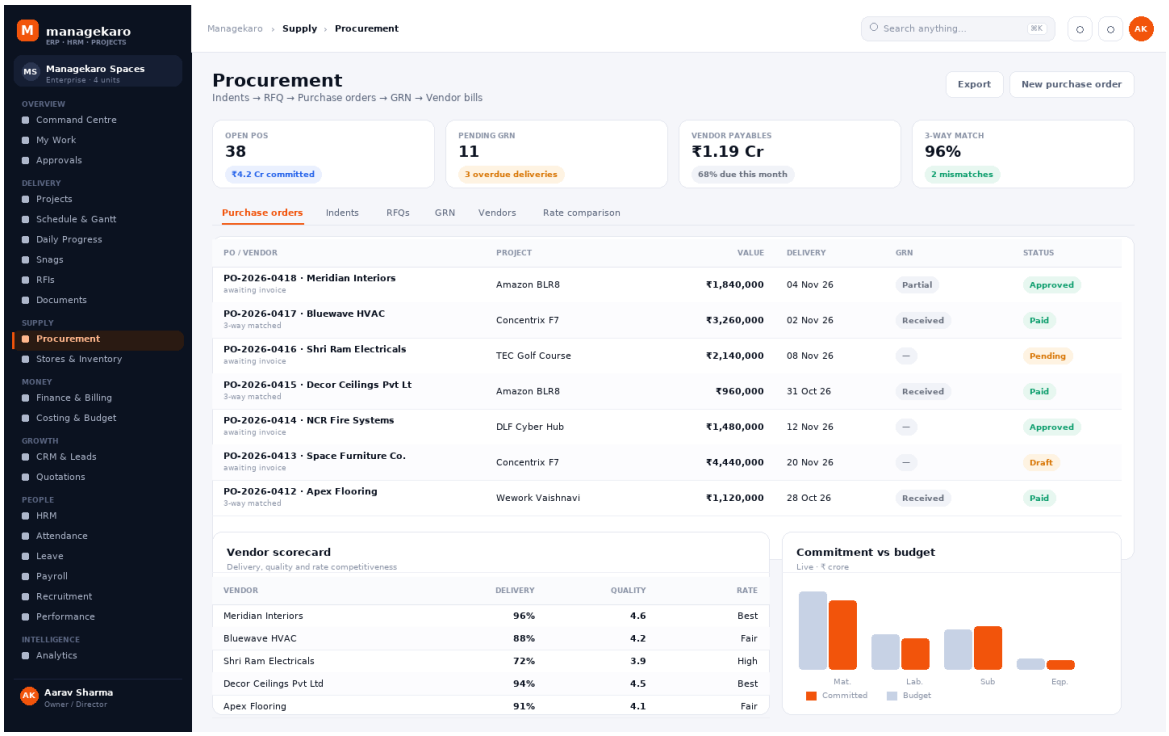


Figure 6.1 — Procurement: POs, three-way match, vendor scorecard and commitment vs budget.

6.2 Raising a requisition

Procurement → New requisition. Pick item from the master (rate auto-fills), quantity, required-by date and justification. Approval routes by amount; approved PRs convert to PO in one click.

6.3 Purchase orders

A PO has multiple lines, GST, delivery date, payment terms, retention % and delivery site. Managekaro checks whether each line is within BOQ budget and flags off-BOQ buying. Releasing a PO creates vendor portal access automatically.

6.4 Receiving material

PO → Receive (GRN). Enter received and rejected quantities per line, choose the store and DC number. Stock is updated, PO received quantity revised, and the invoice becomes eligible for matching.

6.5 Vendors & rate contracts

Vendor records hold GSTIN, PAN, MSME status, bank details, payment terms and a scorecard (on-time %, quality %, documentation). Rate contracts capture negotiated rates with validity and credit days.

6.6 Stores & inventory

Stock is tracked per warehouse with minimum and maximum levels. Issue material to site (outward), receive (inward) or transfer. Low stock and out-of-stock rows are surfaced first.

6.7 Subcontracts

Track scope, value, rate basis, retention, advance and labour count per subcontractor, with progress, billed, paid and compliance validity.

6.8 The five-step chain

1. Indent — site or PM raises a requisition against BOQ lines; approval follows the matrix.
2. RFQ — send to three or more vendors from the vendor master and compare landed rates side by side.
3. PO — convert the winning quote; committed cost posts to the project budget immediately.
4. GRN — stores records receipt (full, partial, rejected); stock and PO status follow.
5. Vendor bill — three-way match (PO ↔ GRN ↔ invoice) before any payment is released.

6.9 Stores & inventory

Multi-warehouse stock with issue-to-project, returns, transfers and reorder levels. Every issue is charged to a project and a BOQ line, so material cost per line is real rather than estimated. Low-stock alerts reach both the storekeeper and the procurement head.

6.10 Vendor scorecards

Delivery reliability, quality rejections, rate competitiveness and dispute count, all computed from transactions. Use it when choosing the next RFQ winner — not gut feel.

6.11 Rate contracts and subcontracts

Fix rates per item and vendor for a period, and POs inherit them automatically. Subcontracts carry scope, retention, mobilisation advance and measurement rules, so sub-contractor bills are checked against contract scope before payment.

07

7. Finance, billing & costing

Project → Commercials → Raise invoice, or Finance → Client invoices → Record receipt. Bill by milestone (mobilisation, 40%, 75%, completion, retention release) with GST. Ageing is calculated from the due date.

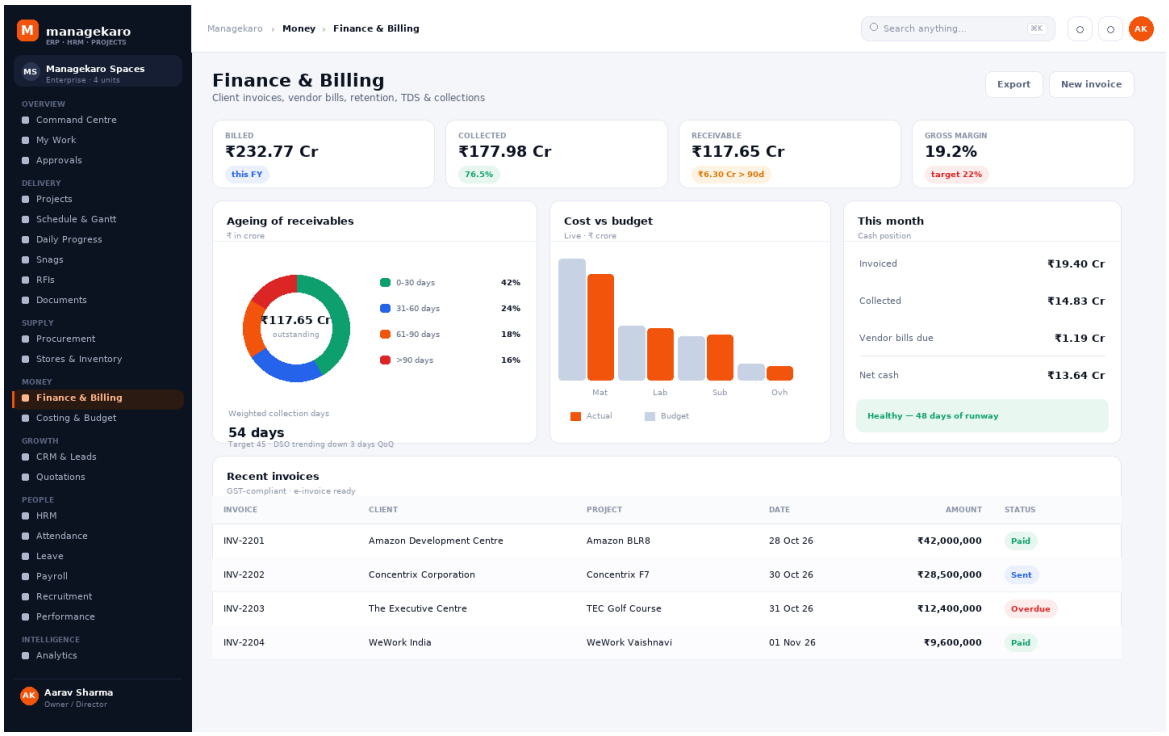


Figure 7.1 — Finance & billing: ageing, cost vs budget, cash position and recent invoices.

7.2 Vendor invoices

Vendor invoices are checked against PO, GRN and measured progress (three-way match). Exceptions are held with a reason. TDS and retention are deducted to arrive at the net payable.

7.3 Payments

Finance → Payments → release with mode (NEFT, RTGS, cheque, UPI) and bank account. The payment is posted against the invoice and the vendor balance updates.

7.4 Site expenses

Capture head (travel, labour, transport, consumables, rental, welfare, safety, courier, printing, misc), amount, mode and bill attachment. Expenses above ₹25,000 route for approval automatically.

7.5 Journal & ledgers

Manual journal entries post to a chosen debit and credit ledger. The trial-balance summary shows receivables, payables, WIP, revenue, retention and net GST. Export is Tally-compatible.

7.6 GST, TDS & compliance

The compliance tab lists GSTR-1, GSTR-3B, TDS 26Q, PF ECR, ESI, PT, labour licence, fire NOC and shop & establishment filings with period, authority, due date and owner.

7.7 Cost & margin

Cost & Margin shows project P&L sorted by weakest margin, revised value (contract + approved variations), budget, actual cost, profit and margin %, plus a leakage table of BOQ lines above budget rate with a negotiate action.

7.8 Client billing by milestone

Billing milestones are defined per project (mobilisation, design freeze, 30% progress, handover…). Certifying a milestone creates a draft invoice with GST, retention and TDS applied; sending it posts a receivable. The ageing view splits outstanding into 0–30, 31–60, 61–90 and 90+ days.

7.9 Costing & margin

- Budget vs committed vs actual per cost head — material, labour, sub-contract and overheads.
- Gross margin from BOQ rates; actual margin after real purchases, labour and overhead allocation.
- Margin-leakage view: BOQ lines above budget rate, wastage, unbilled variations, overtime.
- Project P&L printable per project and consolidated for the portfolio.

7.10 Statutory

GST on invoices (CGST / SGST / IGST), TDS deduction on vendor bills, retention withholding and e-invoice-ready numbering. Every export is CSV so your accountant can post to Tally or Zoho Books; the integrations page can push them automatically.

7.11 Month-end close checklist

1. Confirm every GRN has a matching vendor bill or an open accrual.
2. Certify progress with QS and raise all milestone invoices.
3. Post payroll and record statutory challans.
4. Reconcile bank entries against receipts and payments.
5. Lock the month and export the P&L, cash flow and ageing pack.

08

8. CRM & quotations

Capture company, contact, source (Google, LinkedIn, referral, walk-in, website, WhatsApp, exhibition, existing client), segment, city, indicative value and area. Score and probability drive the weighted pipeline.

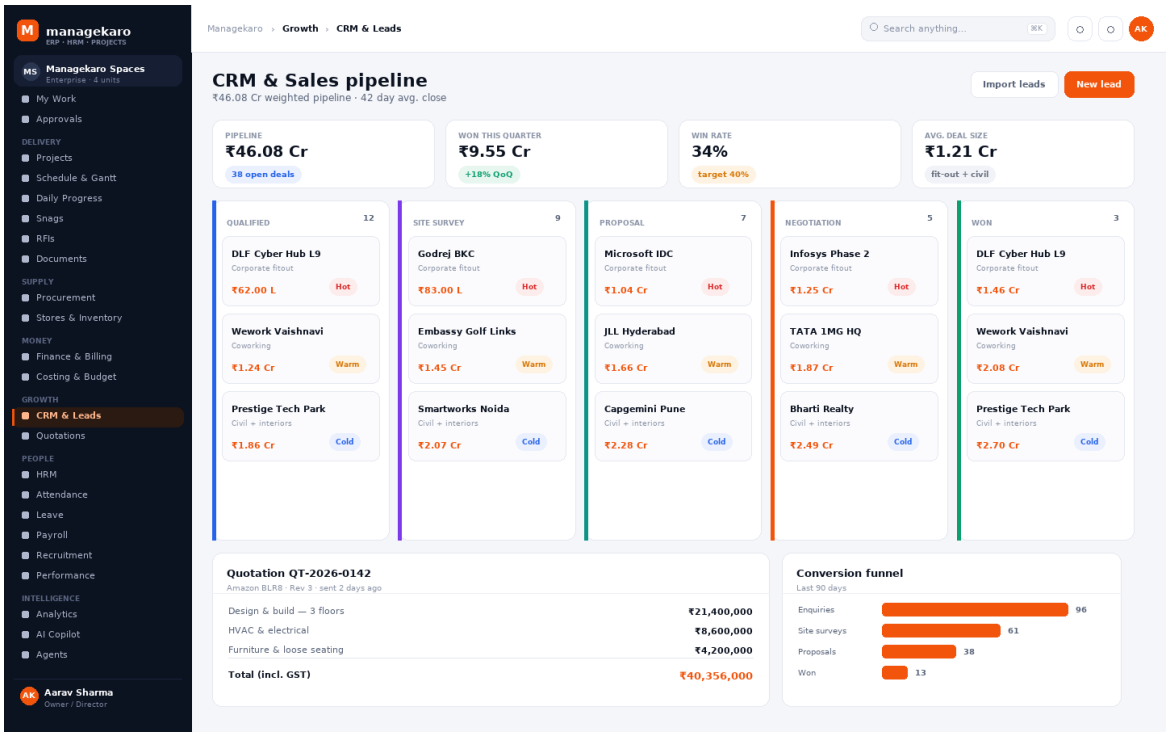


Figure 8.1 — CRM pipeline with deal cards per stage, quotation summary and conversion funnel.

8.2 Pipeline

Six stages: New → Qualified → Site Visit → Proposal Sent → Negotiation → Won. Move a lead by opening it and choosing a stage; probability updates automatically.

8.3 Site visits

Log a visit with purpose (measurement, design brief, feasibility, presentation), date and remarks. Visits appear on the CRM dashboard with the owner.

8.4 Quotations

Create from a template (standard fit-out, design + build, civil only, turnkey retail) with value, margin target, validity and recipient. The PDF-ready preview includes scope, GST, payment terms, timeline and validity.

8.5 Converting to a project

On a Won lead, click "Convert to project". Managekaro creates the project with the lead's value, area, type and city, and you can then import the BOQ.

8.6 Pipeline stages

Qualified → Site survey → Proposal → Negotiation → Won / Lost. Each card carries client, project type, carpet area, estimated value, source and owner. Moving a card forward immediately updates

the weighted pipeline shown on the Command Centre.

8.7 Lead to project in three clicks

1. Log the enquiry (source, site address, area, budget band) and schedule the site survey.
2. Build a quotation from a template: scope lines, rates, margin target and GST. Send as PDF and track revisions.
3. On win, convert — the project is created with the quotation scope as the starting BOQ and the client as the billing party.

8.8 Quotation discipline

Every revision is retained with a timestamp and the margin at that moment, so you can see exactly how much margin you traded away during negotiation.

8.9 Sources that are tracked

Referral, architect / consultant, repeat client, broker, website, campaign, walk-in and cold outreach — each with conversion numbers in the growth analytics tab, so you can stop paying for the sources that never close.

09

9. HRM & payroll

The employee master holds designation, department, role/access, unit, employment type, joining date, gross, statutory IDs (PAN, Aadhaar, UAN, ESI), bank details, skills and leave balances. Adding an employee creates a login.

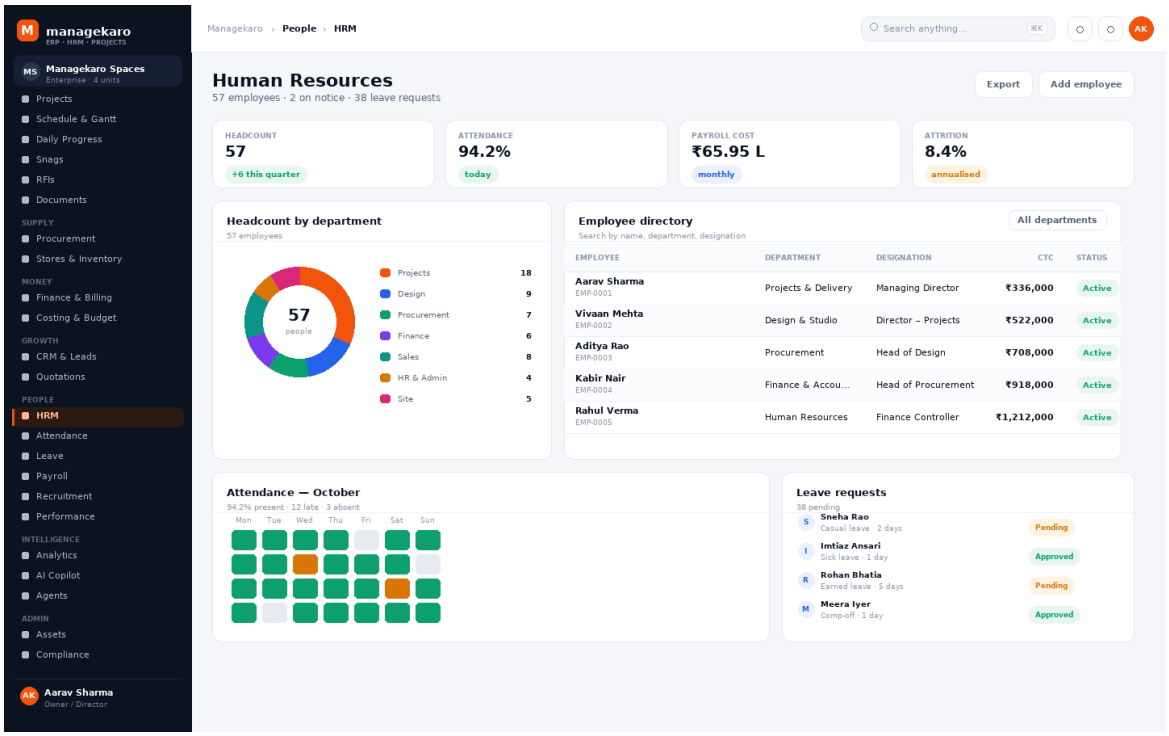


Figure 9.1 — HRM dashboard: headcount split, employee directory, attendance and leave.

9.2 Employee profile

Profile shows salary structure (basic 50%, HRA 40% of basic, conveyance, special), attendance for the month, leave history, recent payslips, appraisal status and skills.

9.3 Attendance

Attendance is geo-fenced: punch-in verifies location (250 m default), optional selfie, shift and grace period. The matrix view shows 14 days per employee with present, late, WFH, leave, half-day, absent and weekly-off colours.

9.4 Leave

Six leave types with entitlement, carry-forward and paid flag. Apply with dates and reason; approval routes manager → HR. Leave beyond balance becomes LOP. Holidays are excluded from computation.

9.5 Payroll

Choose the cycle, verify gross, LOP and overtime, then Run payroll. Components: basic, HRA, conveyance, special allowance, overtime; deductions: PF, ESI, professional tax, TDS and LOP recovery. Payslips are printable and bank files exportable as CSV.

9.6 Recruitment

Post a role (department, location, experience, openings, description), track candidates through Applied → Screening → Interview → Offer → Hired, rate them and hire with one click to create the employee record.

9.7 Performance

Appraisal cycles hold self rating, manager rating, recommended hike, promotion flag and goal completion. Learning & development lists programmes with seats filled and status.

9.8 Attendance & shifts

Geo-fenced check-in from the phone, biometric import, or a manual muster for site labour. Shifts, weekly offs, holidays and overtime are configurable, and late marks or absent days feed payroll automatically.

9.9 Leave

Six leave types with balances (EL, SL, CL, comp-off, maternity, LOP). Requests route to the reporting manager; approved leave updates attendance and payroll. The team calendar shows who is away and when.

9.10 Payroll cycle

1. Lock attendance for the month.
2. Run payroll: gross from the CTC structure, deductions for PF (12%), ESI (0.75%), professional tax and TDS.
3. Review the register and adjust arrears or LOP.
4. Generate payslips (printable, per employee) and the NEFT bank file.
5. File the statutory challans and record the payment.

9.11 Recruitment, appraisals and training

Job openings with a candidate funnel (applied → screened → interview → offer → hired) and one-click hire that creates the employee record and login. Appraisal cycles carry ratings and increments; the training calendar tracks enrolment and completion per department.

9.12 Employee self-service

Each employee sees their own attendance, leave balance, payslips, documents (offer letter, ID proof, policy acknowledgements), appraisal history and timesheets. Managers see their team; HR sees everyone; nobody sees salaries outside their scope.

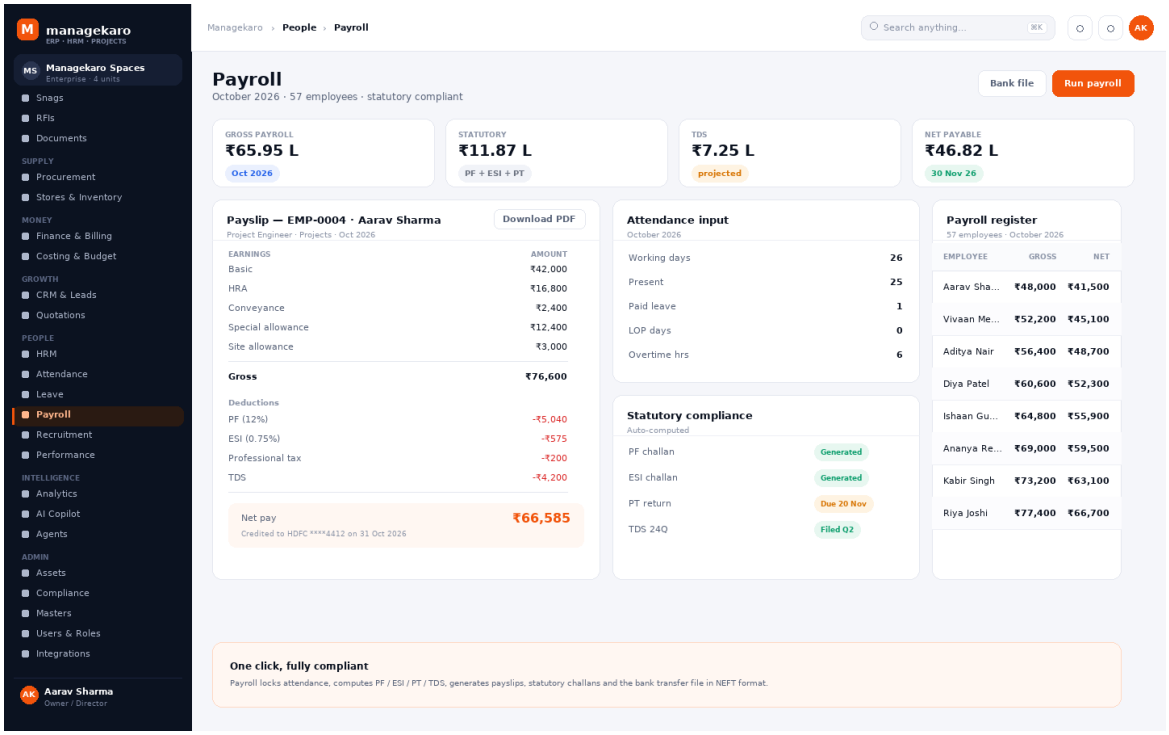


Figure 9.2 — Payroll: printable payslip, attendance input, statutory compliance and pay register.

10

10. Analytics, Copilot & agents

Six dashboard groups: Portfolio (value by type and city, delivery health, progress vs cost, trade heatmap), Project performance (scorecard, S-curve, snag velocity), Financial (cashflow, ageing, cost mix), Procurement (vendor spend and scorecard, GRN quality), People (headcount, utilisation, hours), and Custom dashboards.

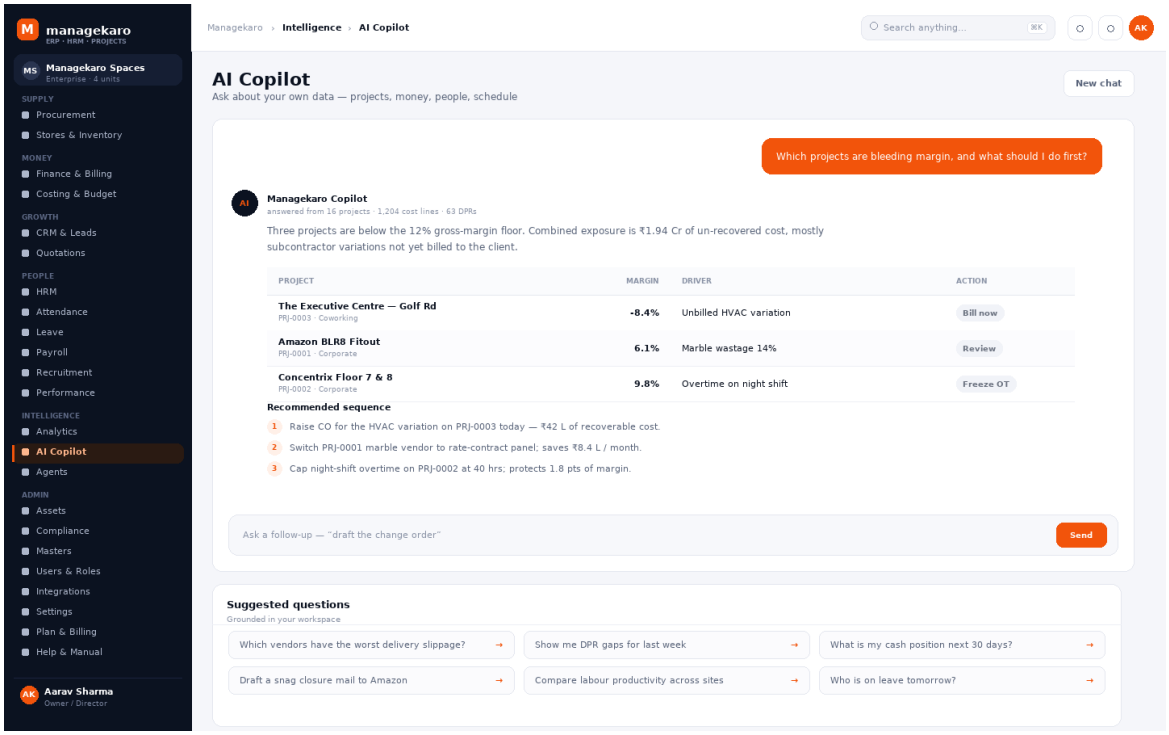


Figure 10.1 — AI Copilot answering from live BOQ, PO, invoice and payroll data with a recommended action plan.

10.2 Copilot

Ask in plain English: "Which projects are bleeding margin?", "How much is outstanding from clients?", "Which vendor is delaying us?", "What is this month's payroll cost?". Answers are computed from your live records, with tables and a suggested action. Export the conversation or start a new one.

10.3 Agents

Analytics, Risk, Reconciliation, Costing, Follow-up and Compliance agents run in the background. They raise findings (slippage, match exceptions, overdue receivables, filings due) and route them to a human approver — agents never approve or pay on their own.

10.4 Configuring agents

Choose what each agent watches and who is notified, and how often. Every run is logged with findings and notifications sent.

10.5 Copilot question patterns that work

- “Which projects are bleeding margin?” — ranks by actual margin and names the driver.
- “What is my cash position in the next 30 days?” — billed, collectable and payables due.

- “Show DPR gaps for last week.” — projects where a site report is missing.
- “Which vendors slip deliveries most?” — vendor scorecard sorted by delay days.
- “Draft a snag closure mail to Amazon.” — built from the open snag list for that project.
- “Who is on leave tomorrow?” — HR calendar across departments.

10.6 Background agents

Six always-on agents watch the workspace: cost overrun, billing lag, snag ageing, low stock, schedule slippage and statutory deadlines. Every finding lands in the risk register with an owner and severity, and surfaces in Analytics → Exceptions.

10.7 Analytics tabs

Executive, Delivery, Commercial, People, Supply chain and Client. Every tab exports CSV and can be scheduled as an MIS email or WhatsApp digest.

10.8 How the answers are computed

The copilot is grounded: it reads the same store the screens read — projects, BOQ, POs, GRNs, invoices, payroll, attendance and snags — then aggregates before answering. That is why numbers in an answer always match the module you click through to, and why “no data” is an honest answer instead of an invented one.

11

11. Admin, masters & billing

Nineteen roles including Owner, System Admin, Project Manager, Site Engineer, Designer, Procurement, Finance, HR, QS, Client portal, Vendor portal and Auditor. Switch personas from the avatar menu to test access.

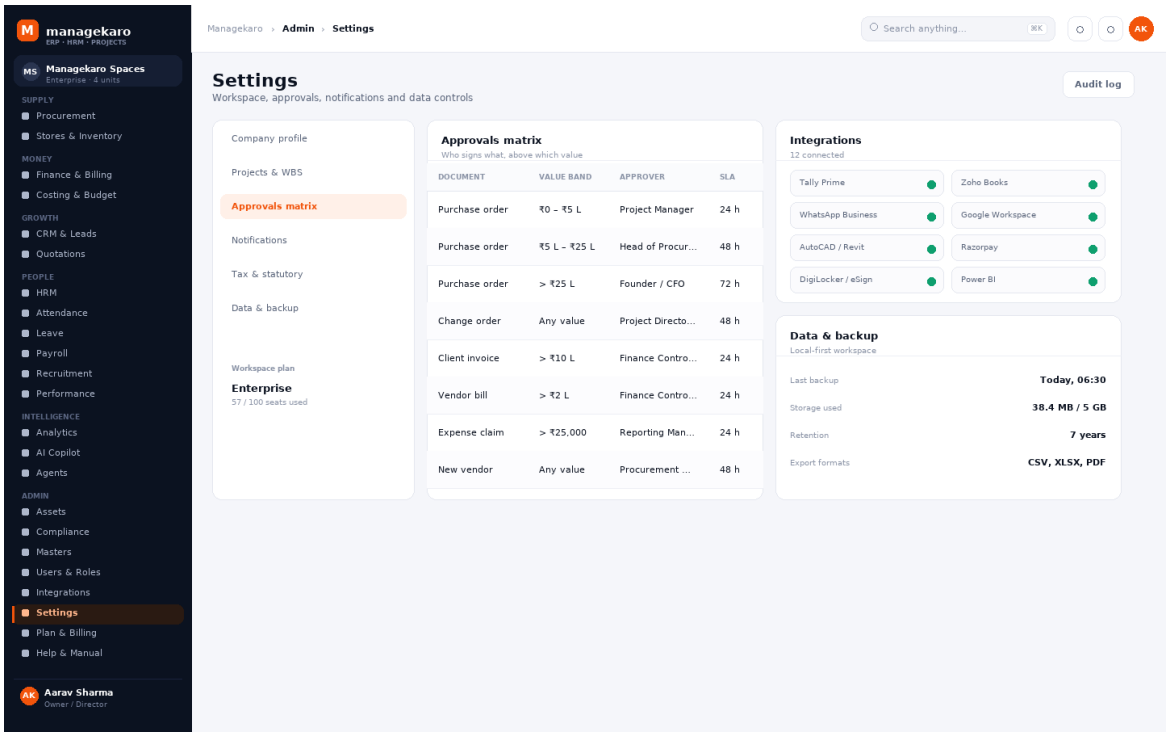


Figure 11.1 — Settings: approvals matrix, integrations and data controls.

11.2 Masters

Item/SKU master (code, trade, unit, standard rate, brand, HSN, GST, specification), clients, business units with GSTINs, departments, tags and templates (BOQ, DPR, snag report, approval matrix, quotation, survey checklist).

11.3 Approval rules

Rules are ordered top-down and first match wins. Example: PO below ₹2 L → PM; ₹2–10 L → PM + Procurement Head; above ₹10 L → PM + Head + Director. Toggle rules on or off without deleting history.

11.4 Integrations

Connect Tally, Zoho, Gmail/Outlook, Drive, MS Project/P6, Razorpay, biometric devices, EPFO/ESIC, Maps, Slack/Teams and AI. Manage webhooks (event → endpoint) and scoped API keys.

11.5 Settings & data

Organisation profile, branding, localisation, units, approval rules, DPR templates, backup (full JSON), CSV exports, audit log and reset.

11.6 Plan & billing

Seats used, storage, add-ons, usage against limits, plan comparison, seat management and GST invoice history.

11.7 Masters to load first

Master	Why it matters
Company & units	Legal entity, GSTIN, state codes, logo — appears on every document
Clients	Billing party, GSTIN, contacts, credit terms
Vendors	Rate contracts, payment terms, category, scorecard history
Items & trades	Units, HSN / SAC, standard rates, reorder levels
Employees & roles	Approval authority, data scope, module access
Templates	BOQ, quotation, DPR, snag and checklist templates

11.8 Users, roles and scope

Nineteen roles ship out of the box — owner, admin, project director, PM, site engineer, QS, procurement, storekeeper, finance, HR, designer, sales, client, vendor and more. Each role has permission patterns per module plus a data scope: own projects, own department or whole company. Client and vendor portals are read-mostly logins limited to their own records.

11.9 Integrations, API and audit

Connect Tally Prime, Zoho Books, WhatsApp Business, Google Workspace, AutoCAD / Revit exports, Razorpay, DigiLocker / eSign and Power BI. Scoped API keys with webhooks let your own systems push leads or GRNs and fetch billing data. The audit log records who changed what, when, with before/after values — filterable by module and user.

11.10 Plan, seats and data

The subscription page shows plan, seats used, invoices and add-ons. Data & backup gives a full JSON export, CSV per module and a one-click reset of the demo dataset.

12

12. Roles: who does what

Site Engineer: DPR (morning punch-in, evening report), GRN on delivery, raise snags, update activity progress. QS: measurement book, certify executed quantity, prepare client billing. Procurement: convert approved PRs to POs, chase delivery, maintain rate contracts. Finance: match invoices, run payments, chase receivables. PM: review delay register, close snags, approve site expenses. HR: attendance exceptions, leave approvals, payroll cycle. Director: approvals inbox, cost & margin, cash position.

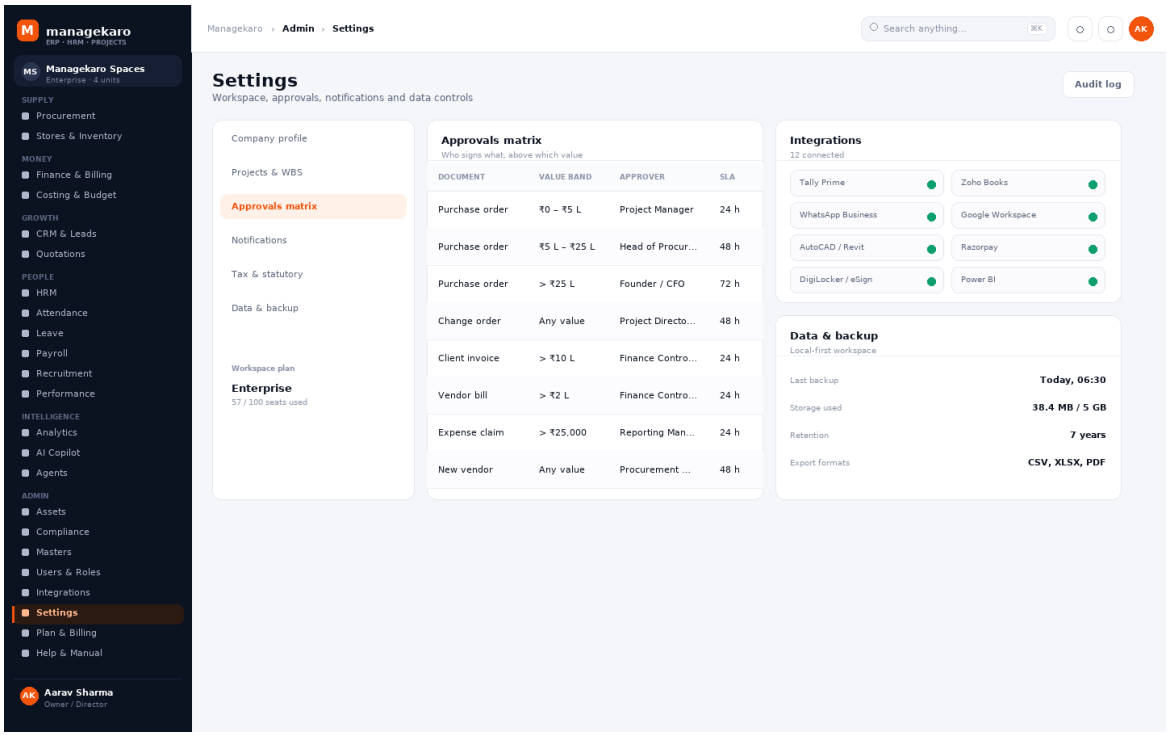


Figure 12.1 — The approvals matrix is where roles become real: who signs what, above which value.

12.2 Approval matrix (default)

Purchase Order: ₹0–2 L PM; ₹2–10 L PM + Procurement Head; ₹10 L+ PM + Head + Director. Vendor invoice: 3-way match then QS + Finance. Change order: QS → PM → Client. Expense above ₹25,000: Site Engineer → PM → Finance. Leave above 3 days: Manager → HR.

12.3 Client & vendor portals

Clients see progress, drawings, client-facing snags and invoices, and approve variations. Vendors see their POs, delivery schedule, GRN acknowledgements and invoice status. Both are read-scoped and cannot see other clients or vendors.

12.4 A week in the life

Role	Monday	Wednesday	Friday
Founder	Command Centre + approvals above ₹25 L	Margin review on two critical projects	Cash and billing forecast

Role	Monday	Wednesday	Friday
Project Manager	Schedule review, assign snags	Client walkthrough, DPR review	Certification pack to QS
Site Engineer	Submit DPR with photos	Raise snags and a material indent	Verify GRN, close snags
QS	Update executed quantities	Raise change orders	Milestone certification
Procurement	Clear indents, float RFQs	Compare rates, release POs	Chase deliveries, review vendors
Finance	Raise invoices, chase overdue	Three-way match vendor bills	Cash position, GST / TDS check
HR	Attendance exceptions	Interview panel, offers	Payroll inputs, leave approvals

12.5 Permission patterns

View, create, edit, approve and delete — per module, per role, with amount ceilings on approvals. A site engineer can raise an indent but not approve it; a PM approves up to ₹5 L; finance posts payments but cannot create projects. Client users see only their own project's progress, snags and invoices.

12.6 Switching persona in the demo

From the sign-in screen pick Director, PM, Procurement, Finance, Site Engineer or HR Manager. Menus, approval authority and data scope change with the persona, which is the fastest way to show a department what they will actually see.

13

13. Desktop app & deployment

Download Managekaro-Setup-1.0.0.exe from the download page. It is a native 64-bit Windows executable that works on Windows 10, 11, 8.1 and Server 2016+. Double-click to run; if SmartScreen warns, choose More info → Run anyway. The app opens the workspace in your default browser; data stays in local storage on that machine.

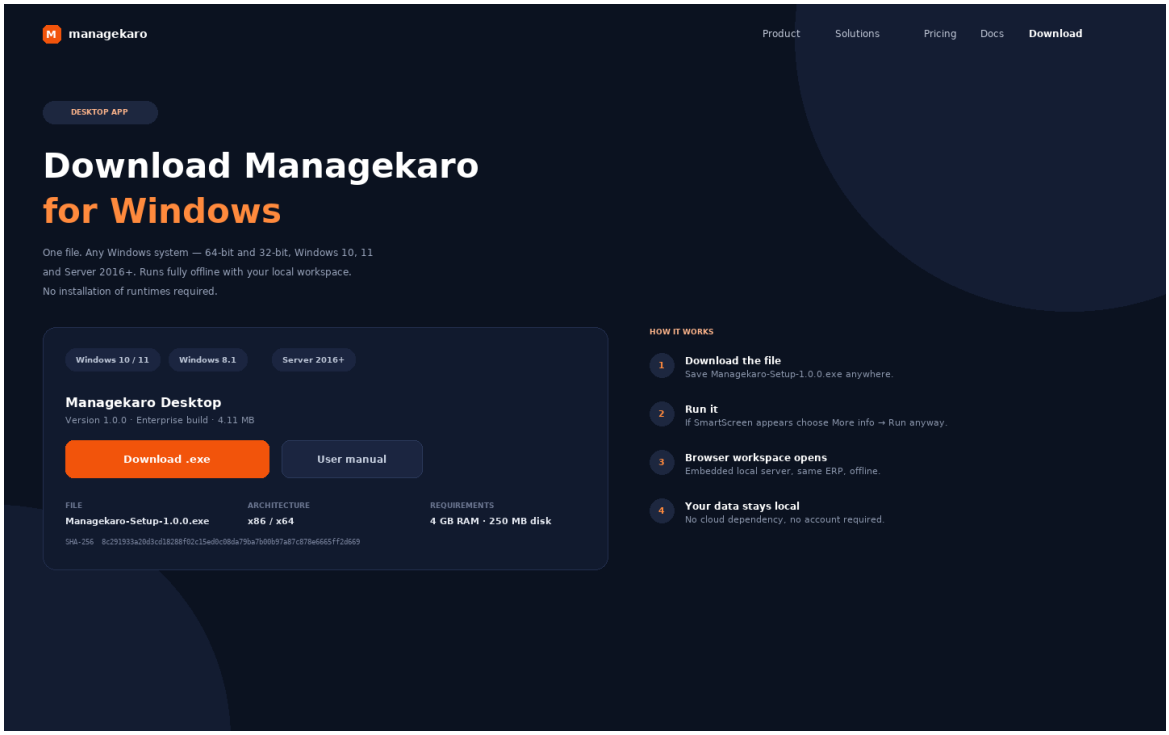


Figure 13.1 — The download page and the single-file Windows build it distributes.

13.2 Web deployment (Vercel)

The workspace is a static site — no build step. Push the repository to GitHub, import it in Vercel, keep the framework preset as "Other" and leave the build command empty. vercel.json already sets headers, rewrites and caching. The site is live at your vercel.app domain and every push redeploys automatically.

13.3 Offline & local hosting

Because it is static, you can host it on any web server, an intranet share or even open index.html from disk. For a shared team workspace, enable a backend (see 13.4) so data is not limited to one browser.

13.4 Data & production notes

This build ships with a deterministic demo dataset persisted to browser local storage. To run it as a multi-tenant SaaS, connect the store layer (assets/js/core/store.js) to your API: the CRUD methods (list, add, update, remove) and the session helpers are the only integration points, so screens stay unchanged.

13.5 Running the Windows build

1. Download Managekaro-Setup-1.0.0.exe from the Download page.

2. Double-click it. If SmartScreen appears, choose More info → Run anyway — the build is not code-signed.
3. The launcher unpacks the app to %LOCALAPPDATA%\\Managekaro\\app-1.0.0, starts a local server on 127.0.0.1 and opens your default browser.
4. Keep the console window open while you work; closing it stops the local server. Data lives in that browser's local storage.

A 32-bit build (Managekaro-Setup-1.0.0-x86.exe) is published alongside for older machines. Compare the SHA-256 shown on the download page against the published .sha256 file before running.

13.6 Deploying the web app

The web app is a static bundle — no build step, no server runtime. On Vercel, import the repository and keep the root as the output directory; the included vercel.json handles clean URLs (/download, /app, /login, /docs), cache headers and security headers. Any static host works the same way. Locally run npm start and open http://localhost:5173.

13.7 Data, backup and reset

The demo persists to browser local storage under managekaro.db.v15. Settings → Data & backup exports the whole dataset as JSON and can reset it to the deterministic seed. A production deployment swaps the store for an API — module code reads through MK.store, so no screen logic changes.

13.8 Publishing a new build

Run node tools/desktop/build.js to compile the launcher, embed the current web assets and write the installer plus its SHA-256 file into downloads/. Run node tools/smoke.js first: it boots the app headlessly, walks all 48 routes and fails on any missing asset or runtime error.

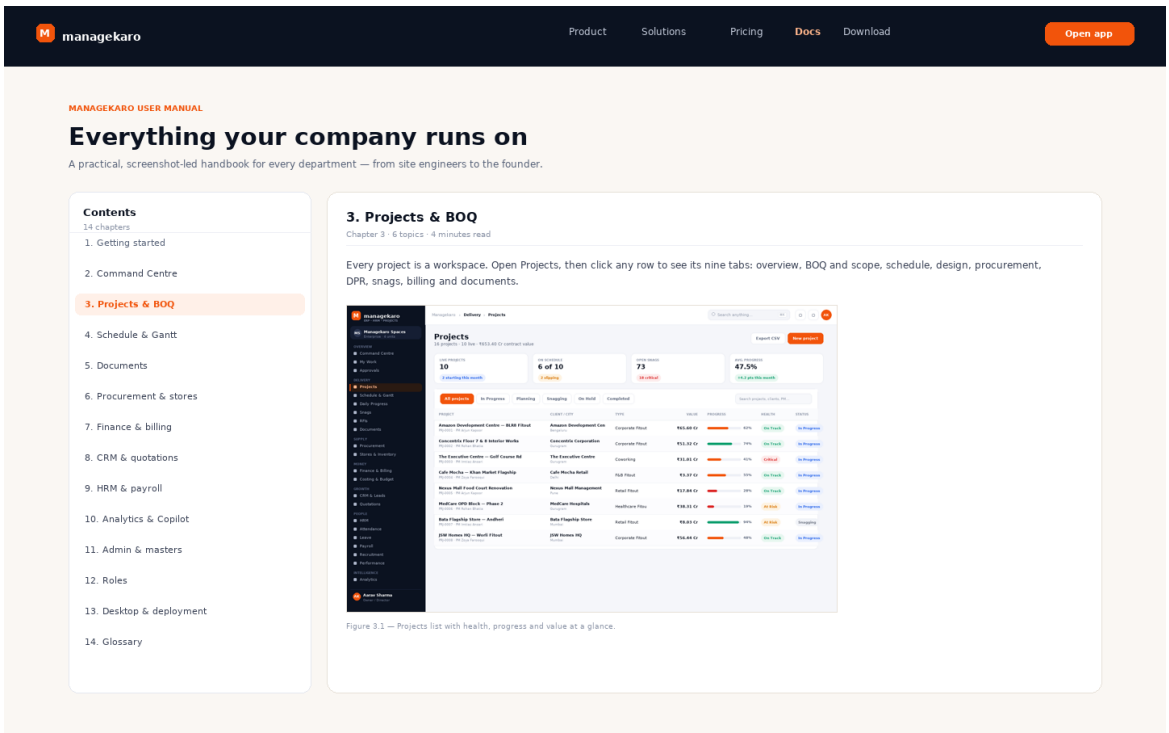


Figure 13.2 — This manual rendered in the browser, printable to PDF in one click.

14

14. Glossary & shortcuts

BOQ — bill of quantities. WBS — work breakdown structure. PR — purchase requisition. PO — purchase order. GRN — goods receipt note. DPR — daily progress report. RFI — request for information. CO — change order. NCR — non-conformance report. Retention — amount withheld until defect-liability period ends. TDS — tax deducted at source. LOP — loss of pay. GFC — good for construction.

14.2 Shortcuts

⌘/Ctrl + K opens the command palette (pages, projects, people, vendors, actions). Esc closes any overlay. In the palette, ↑/↓ move and Enter opens. Settings → Data exports a full JSON backup at any time.

14.3 Troubleshooting

Screen appears empty — reset demo data from Settings → Data. Numbers look stale — data is stored per browser; use a single browser profile per demo. PDF print cuts cards — use the print button on the page header, not the browser menu. Excel shows one column — open CSV via Data → From Text and pick comma delimiter.

Appendix A

Feature book — everything included

One workspace covering the full operating model of a fit-out and construction company.

Delivery

Project control from award to handover: one project workspace links scope, schedule, cost and quality.

- Projects with type, city, contract value, health, PM, client and nine tabs per project
- BOQ with WBS codes, trades, units, rates, executed quantities and rate variance per line
- Change orders with justification, client approval, approval matrix and automatic BOQ impact
- Activity schedule with baseline, dependencies, milestones, delay register and critical path
- Gantt with drag-to-reschedule, planned vs actual S-curve and slipping-activity markers
- Daily progress reports with manpower by trade, work done, material received, blockers and photos
- Snag list with trade, location, priority, owner, due date and photo proof of closure
- RFIs to consultants with due dates, answers and drawing-revision linkage
- Drawing register with revisions, GFC status, pin comments and superseded history
- Handover pack: as-built drawings, O&M manuals, warranties, test certificates and closure evidence

Commercials & supply chain

Every rupee committed, received and billed is traceable to a project and a BOQ line.

- Indents raised against BOQ lines with approval hierarchy
- RFQs to multiple vendors with side-by-side rate comparison
- Purchase orders that post committed cost to the project budget immediately
- GRN with full, partial and rejected receipts; stock and PO status update together
- Three-way match (PO, GRN, vendor invoice) before payment release
- Rate contracts and subcontracts with retention and mobilisation advances
- Multi-warehouse inventory with issue-to-project, returns, transfers and reorder levels
- Vendor master with scorecards for delivery reliability, quality and rate competitiveness

Finance & billing

Receivables, payables, statutory and margin in one ledger, closed monthly without spreadsheet reconciliation.

- Client billing by milestone with GST, retention and TDS applied automatically
- Invoice register with due dates, ageing buckets and collection status
- Receivables ageing 0-30 / 31-60 / 61-90 / 90+ with weighted collection days

- Vendor bills, payment scheduling and expense claims with approval limits
- Budget vs committed vs actual per cost head, project P&L and portfolio consolidation
- Margin leakage report: BOQ lines above budget rate, wastage, unbilled variations and overtime
- Cash position forecast with runway, month-end close checklist and lock
- Every export is CSV and pushable to Tally Prime or Zoho Books

Growth

Pipeline discipline from first enquiry to a signed contract, with margin held through negotiation.

- Lead capture from referral, consultant, repeat client, broker, website, campaign, walk-in and cold outreach
- Six-stage pipeline with weighted value, source conversion and average days to close
- Site survey scheduling with area, budget band and scope notes
- Quotation templates with scope lines, rates, margin target and GST
- Revision history that records the margin traded away at each round
- One-click conversion of a won quotation into a project with its BOQ

People (HRM)

One attendance and payroll engine for staff and site labour, fully statutory.

- Employee master with statutory IDs (PAN, UAN, ESI), bank details and CTC structure
- Geo-fenced mobile attendance, biometric import and manual muster
- Shifts, weekly offs, holidays, overtime, late marks and LOP
- Six leave types with balances, manager approval and team calendar
- Payroll with PF, ESI, professional tax and TDS; printable payslips and NEFT bank file
- Recruitment funnel with one-click hire that creates the employee record and login
- Appraisal cycles with ratings and increments; training calendar with enrolment
- Employee self-service for payslips, documents, leave and timesheets

Intelligence

Answers computed from live transactions, not typed summaries.

- Command Centre with portfolio KPIs, health split, cash and pending approvals
- Analytics with six tabs: executive, delivery, commercial, people, supply chain, client
- Exception engine for cost overrun, billing lag, snag ageing, low stock and slippage
- AI Copilot that answers questions over projects, BOQ, POs, invoices, payroll and snags
- Six background agents writing into a risk register with owners and severity
- Scheduled MIS packs by email or WhatsApp

Platform & admin

Enterprise controls without enterprise complexity.

- Nineteen roles with per-module permissions and amount ceilings on approvals
- Amount-based approval matrix with SLA tracking and delegation
- Client portal and vendor portal logins limited to their own records
- Masters for company, units, clients, vendors, items, trades, templates
- Integrations: Tally Prime, Zoho Books, WhatsApp Business, Google Workspace, AutoCAD/Revit, Razorpay, DigiLocker/eSign, Power BI
- Scoped API keys and webhooks for your own systems
- Audit log with before/after values, filterable by module and user
- JSON backup, per-module CSV export and demo-data reset

Apps & deployment

The same workspace on every device, including site offices with no connectivity.

- Web workspace delivered as a static bundle, deployable to Vercel with clean URLs
- Installable PWA for phones with DPR, GRN, snag and attendance shortcuts
- Native Windows desktop executable (64-bit and 32-bit) with the whole app embedded
- Offline local mode that needs no runtime, no admin rights and no account
- Print-ready documents: payslips, invoices, BOQ, project P&L and this manual

Appendix B

Company profile used in the demo

Projects	16 total · 10 live · 3 completed
Contract value	₹653 Cr
Billed / collected	₹233 Cr / ₹178 Cr
Gross margin	19.2% (actual 10.0%)
Headcount	57 employees · 2 on notice
Snags	73 open · 18 critical
Pipeline	₹46.08 Cr · won ₹9.55 Cr

Support

Email **help@managekaro.com** · phone **+91 124 480 9100** · four working hours response. Enterprise customers get a named CSM and a shared support channel inside the workspace.
